MILESTONE 2 REPORT

Scheduling and Design

Student Mentoring and Career Support Platform

Team 032 – Himalayan Coders | IIT Madras | Problem Statement 2

Prepared by: Ankur Maurya · Adnan Mustafa · Himanshu Rathor · Hemendra Kumar Sharma · Bojannagari Pavan Kumar Reddy

Draft for team review — dates, meeting times, owners, and sample data must be confirmed by the team.

Document Status and Project Purpose

This proposed package is based on the supplied Milestone 2 requirements and the available Milestone 1 project context. The dates and meeting times are planning assumptions. The Project Manager and Scrum Master must discuss the schedule with the whole team before finalizing it. Frontend screenshots are static prototype mockups, not screenshots of a deployed or backend-connected application.

The platform supports students in describing mentoring needs, tracking requests, viewing a client-assigned connection, and providing feedback. Mentors maintain their own professional profiles and availability. Coordinators/admins manage mentor information, assign matches, review requests, and identify delays. The design follows client-mediated matching: students do not browse all mentor profiles directly.

1. Design of Components

Component	Responsibilities	Notes
Student UI	Dashboard, goals/profile, request status, assigned connection, feedback	No public mentor directory
Mentor UI	Edit background, qualifications, skills, expertise and availability	Mentor edits own profile
Coordinator/Admin UI	Review student needs, maintain mentor records, assign matches, monitor delayed cases	Role-restricted actions
API / workflow layer	Authentication, authorization, validation, status transitions, audit events	Proposed; not implemented
Data layer	Persist students, mentors, requests, availability, sessions and feedback	Relational database proposed
Notifications	Email/in-app updates for assignments and reminders	Confirm with client first

Interaction: browser UI → authenticated API → validation/workflow services → relational database. Enforce role-based permissions server-side; hiding a UI link is not security.

2. Class Diagram

Conceptual diagram; validate the class names and relationships against the final user stories before implementation.

Conceptual Class Diagram



Students can submit many requests. Mentors maintain a profile and availability slots. A request may lead to a session and optional feedback. Administrative actions should be authorized and auditable.

3. Database Design

Logical Database Design (ERD overview)



Table	Key fields / constraints	Purpose
STUDENT	PK student_id; email UNIQUE; programme_level; goals; skills	Student profile and needs
MENTOR	PK mentor_id; email UNIQUE; qualifications; experience; profile_status	Mentor profile and review status
ADMIN_USER	PK admin_id; email UNIQUE; role; active	Coordinator/admin access
MENTORING_REQUEST	PK request_id; FK student_id; FK assigned_mentor_id NULL; topic; status; submitted_at	Request workflow

Table	Key fields / constraints	Purpose
AVAILABILITY_SLOT	PK slot_id; FK mentor_id; day; start/end; timezone	Mentor availability
SESSION_FEEDBACK	PK session_id; FK request_id UNIQUE; scheduled_at; outcome; rating; comments	Session and feedback
AUDIT_EVENT (recommended)	PK event_id; actor_id; action; entity_type/id; created_at	Track key admin changes

Use foreign keys, uniqueness constraints, timestamps and agreed status values. Confirm retention, privacy, timezone, and authentication requirements before implementation.

4. Sprint Schedule

Proposed 6-week window: 2 November–11 December 2026. The team must confirm capacity, dependencies and dates before committing.

Sprint	Dates (proposed)	Scope	Exit criteria
Sprint 0: Align & design	2–6 Nov	Confirm stories, roles, architecture, diagrams, GitHub issues and acceptance criteria	Scope/design baseline reviewed
Sprint 1: Core UI	9–20 Nov	Student dashboard, request tracking, mentor profile editor, navigation, responsive styling	Linked pages reviewed; screenshots captured
Sprint 2: Coordinator & data	23 Nov–4 Dec	Coordinator dashboard, database/API contracts, validation and access-control design	Data and component flows reviewed
Hardening & submission	7–11 Dec	Integration review, testing, UI fixes, report, screenshots, README/ZIP	Team review and package ready

Roles and Definition of Done

Project Manager / Scheduling Lead: timeline and dependencies. **Scrum Master / Co-Lead:** cadence, blockers and actions. **Design Lead / Backend Developer:** diagrams and API/data design. **Frontend Developer(s):** linked pages on feature branches. **Code Reviewer:** to be assigned by the team. Done means acceptance criteria met, issue and PR linked, reviewer comments addressed, UI checked, documentation updated, and no secrets/real personal data committed.

5. Scrum Meetings Schedule and Minutes

Meeting	Cadence	Proposed time (IST)	Output
Sprint Planning	First day of each sprint	Monday 7:30–8:15 PM	Sprint goal, stories, owners, acceptance criteria
Async stand-up	Weekdays	Post by 10:00 PM	Yesterday/today/blockers
Sprint Review	Last Friday of sprint	7:30–8:00 PM	Demo and stakeholder feedback
Retrospective	After review	8:00–8:30 PM	Improvement actions and owners
Backlog refinement	Mid-sprint Wednesday	7:30–8:00 PM	Clarify and estimate upcoming work

Minutes template

Date / meeting: [fill in] **Attendees:** [fill in] **Facilitator:** [fill in]
Sprint goal: [fill in]
Decisions: [decision, owner, rationale]
Progress: [completed / in progress / blocked]
Blockers / risks: [issue, impact, owner, due date]
Actions: [action, owner, due date]
Next meeting: [date/time]

Kickoff agenda to record after meeting

Confirm scope, role assignments, Sprint 0 dates, repository branch strategy, review process and client questions. Record actual decisions only after the meeting. Open items include code reviewer assignment, profile verification, status transitions, readiness response, unsuitable-match review, privacy and retention.


6. Gantt Chart

Proposed timeline; confirm dates and assign named owners before treating it as committed.



7. Kanban Board


This is an example board. Recreate it in GitHub Projects, assign owners and update statuses. Link each pull request to a GitHub Issue.

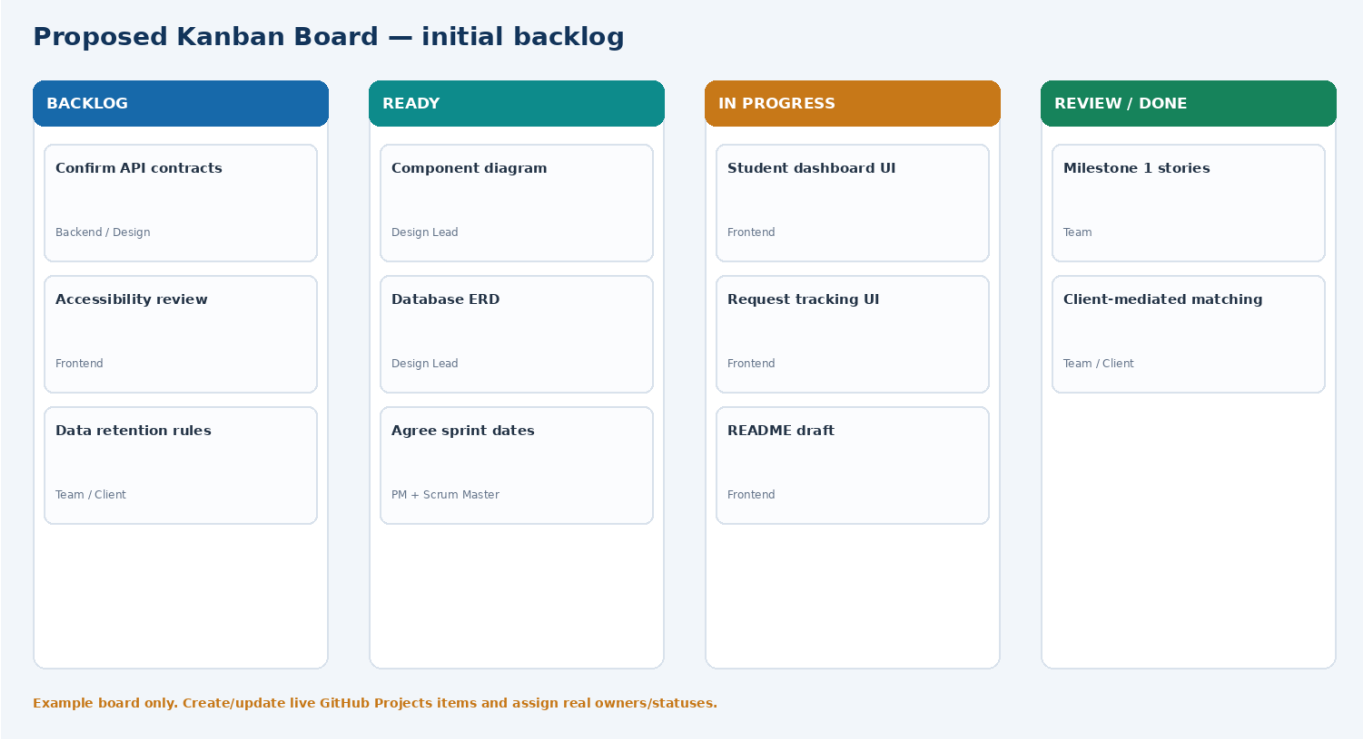


8. Frontend Screenshots

These are static UI prototype mockups, not screenshots of a deployed application. Replace with genuine browser screenshots after the pages are implemented and tested.


8.1 Student dashboard

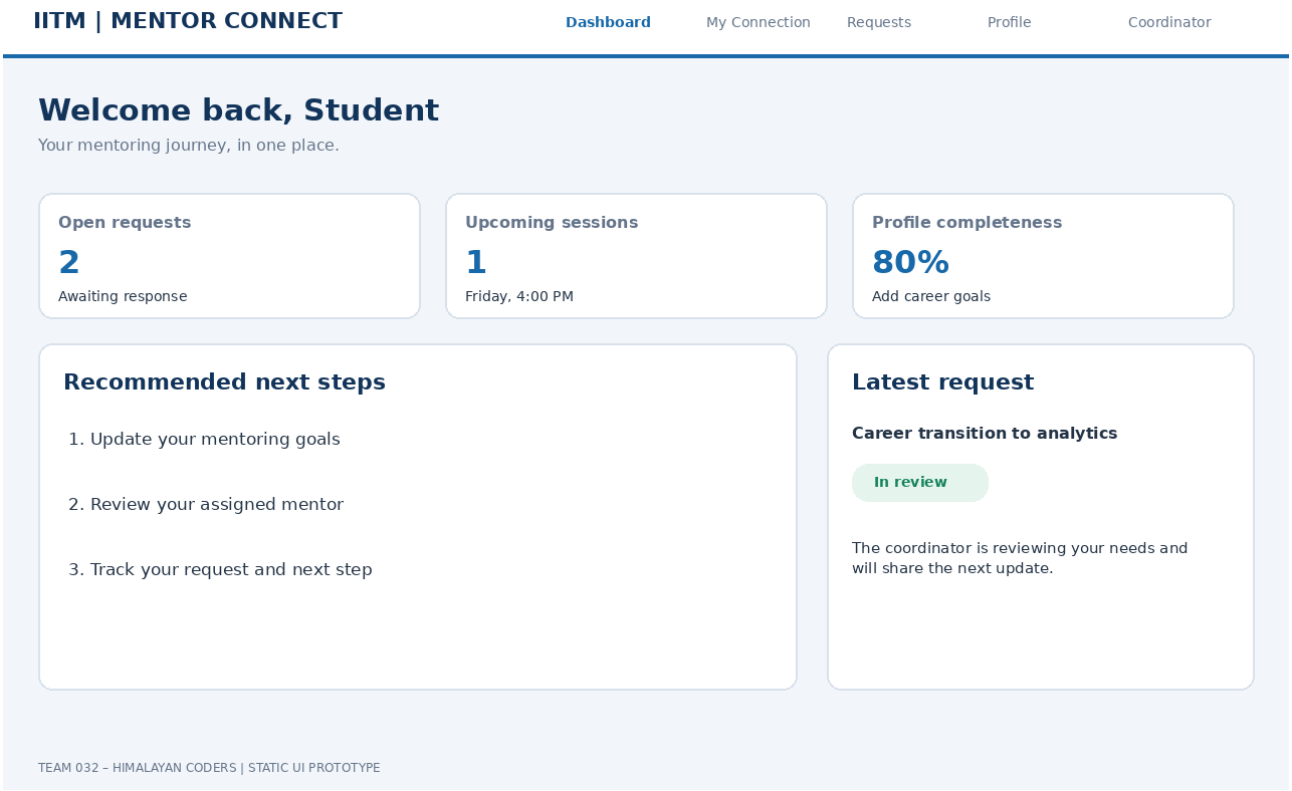


8.2 Assigned mentor connection

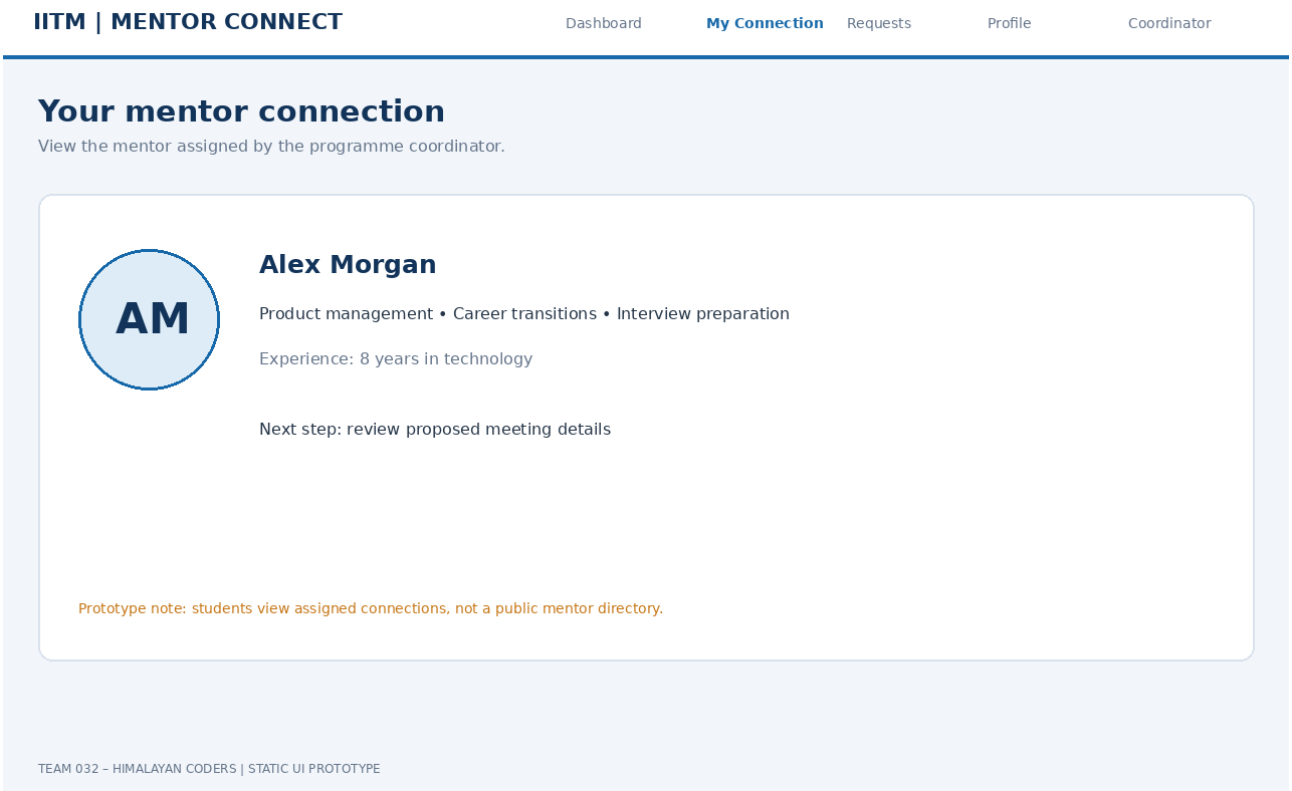


8.3 Request tracking

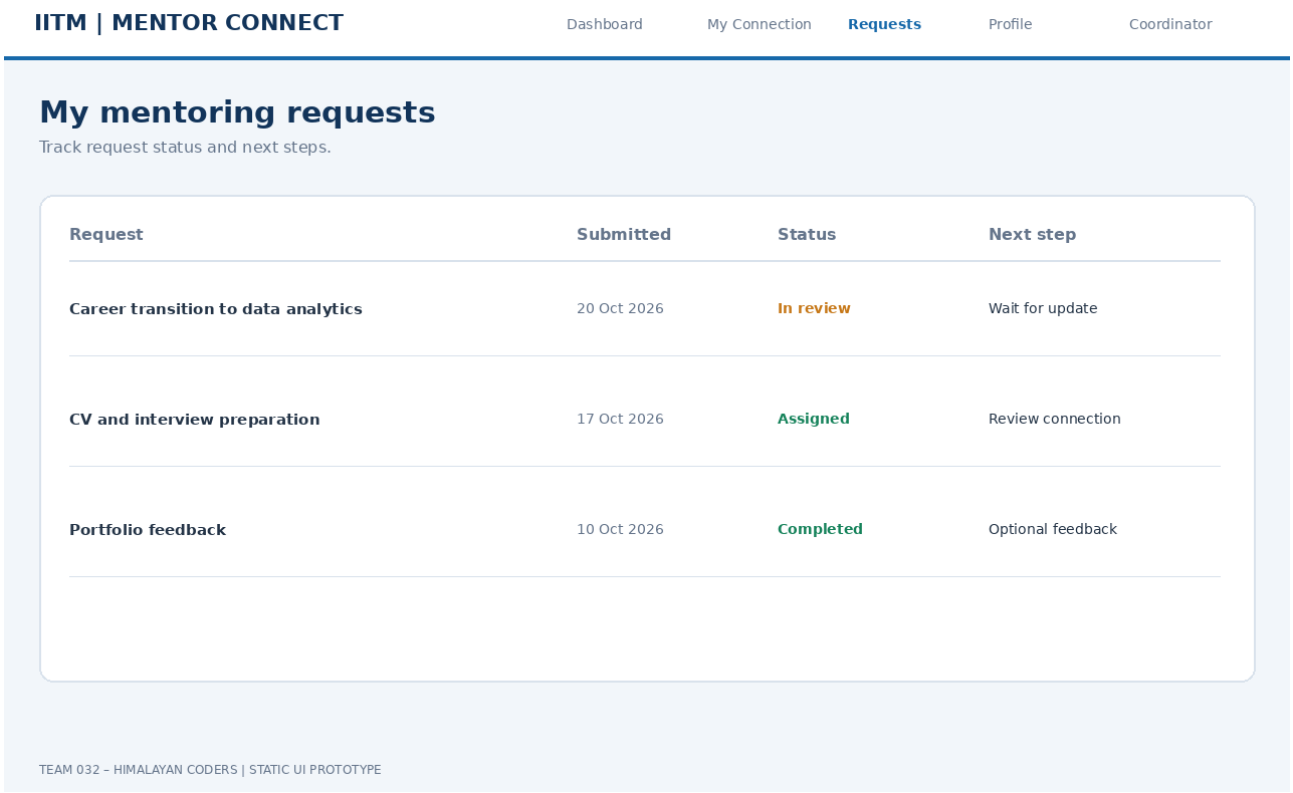

8.4 Mentor profile editing

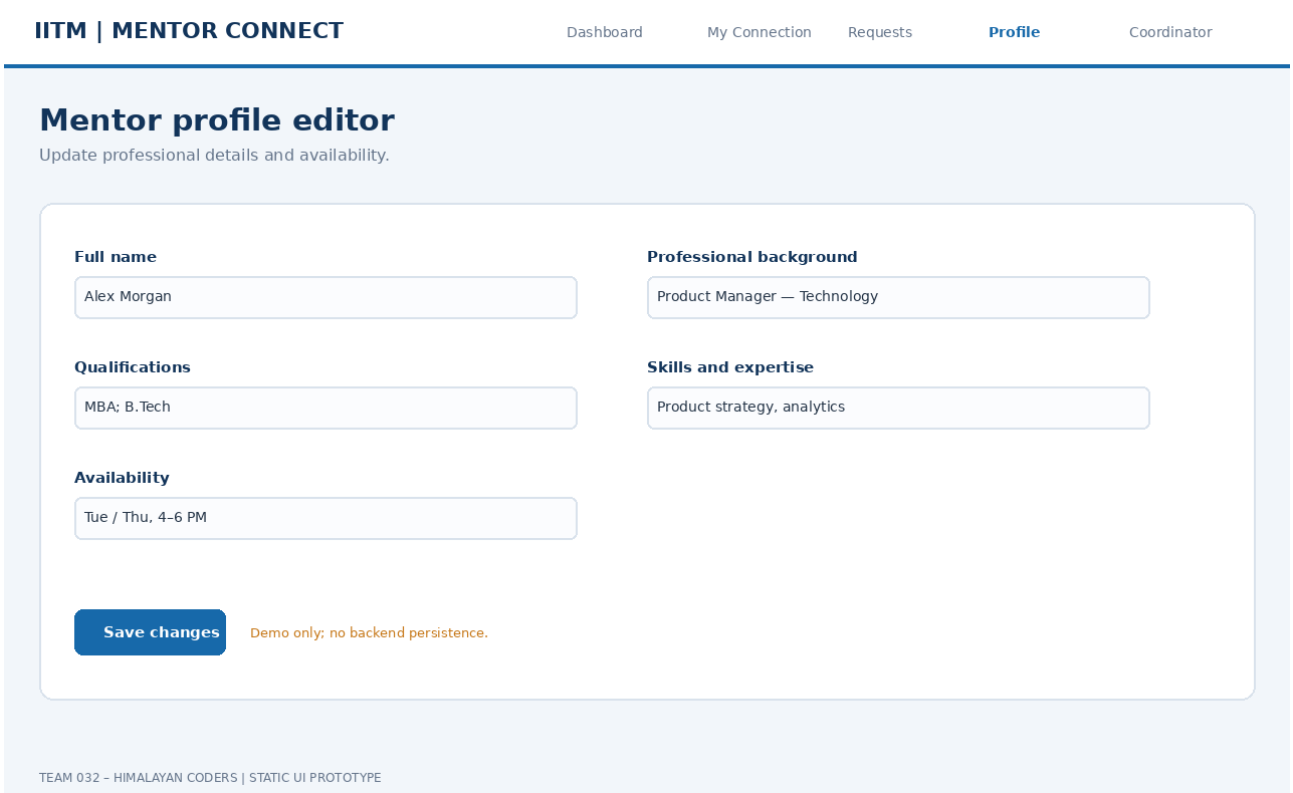

8.5 Coordinator dashboard

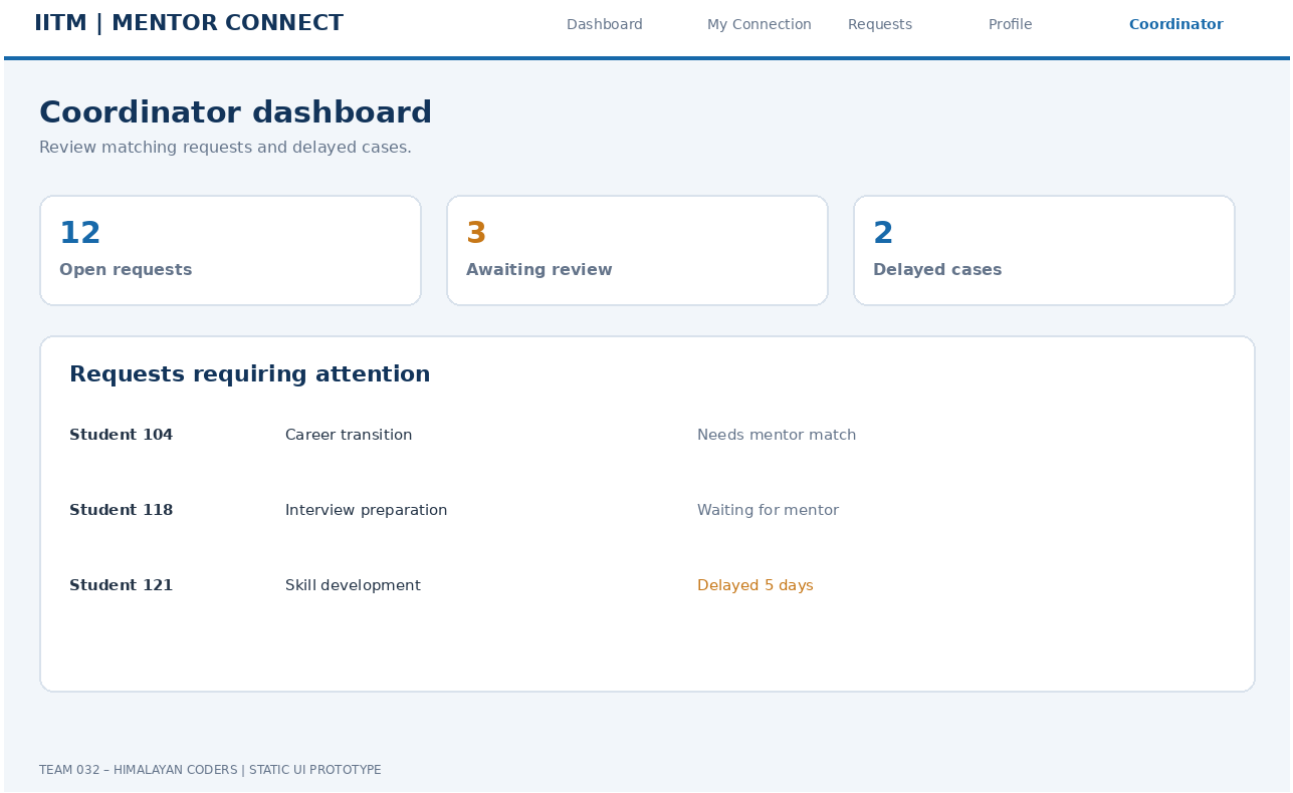
IITM | MENTOR CONNECT
Dashboard
My Connection
Requests
Profile
Coordinator
Coordinator dashboard
Review matching requests and delayed cases.
12
Open requests
3
Awaiting review
2
Delayed cases
Requests requiring attention
Student 104
Career transition
Needs mentor match
Student 118
Interview preparation
Waiting for mentor
Student 121
Skill development
Delayed 5 days
TEAM 032 – HIMALAYAN CODERS | STATIC UI PROTOTYPE

9. Frontend Code Package and README

The ZIP contains five linked HTML pages and a shared stylesheet. Unzip, open the frontend folder, and open index.html in a modern browser. No package installation is required. The prototype uses sample data and has no backend, database, authentication or persistence. The profile form shows a demo confirmation only.

10. Risks, Dependencies and Open Questions

• Confirm profile edit permissions and administrator/mentor roles.
• Confirm request status transitions, student readiness response and unsuitable-match/rematch path.
• Confirm whether sessions are scheduled directly or coordinated externally.
• Define mentor-field visibility and student privacy.
• Confirm notification channels and consent.
• Agree data retention and audit requirements.
• Confirm frontend/backend stack, database, hosting and authentication.
• Confirm team availability, sprint dates and code reviewer.

11. Submission Checklist

■ Component design included
■ Class diagram included
■ Database design included
■ Sprint schedule included
■ Scrum meeting schedule and actual minutes added
■ Gantt screenshot included
■ Live Kanban screenshot added
■ Real frontend screenshots substituted for mockups
■ Frontend ZIP and README included
■ Code reviewer assigned
■ Team approved schedule
■ TA/client feedback recorded
